

# Weekly Blitz

June 30, 2017




## *Pleasant Run Elementary*



The gymnasium is up to fourteen feet. Temporary lighting and decking have been installed in lower level B. The main level in Area B, is scheduled for pour July eleventh.

# White Oak Middle School

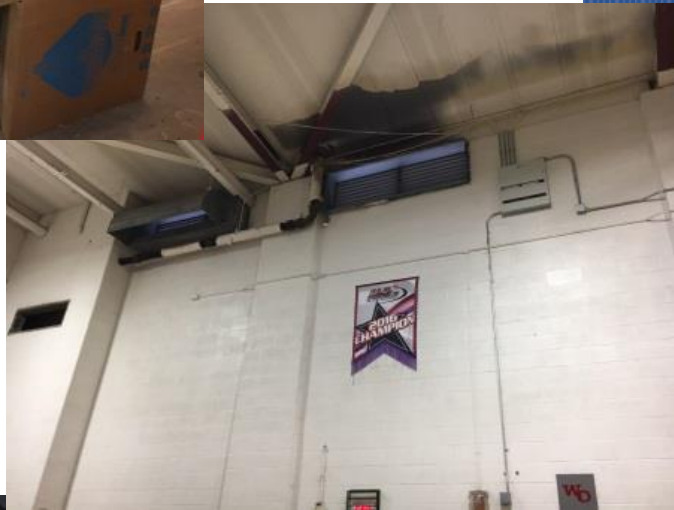

The new switch gear box has been installed: tie in to follow. While, old duct work was removed to make room for newer. Lastly, insulation was placed around the new chiller pipes.

# Taylor Elementary



In preparation for the main level pour (July 12, 2017) in Area B, handrail was installed. Following bar joist and I-Beam installation, decking was placed on to main level B. The gymnasium reached four feet in Area A, with grouting to follow July fifth.

# Struble Elementary



Steel Decking installation has progressed on Main Level Area B. Masonry work has also moved forward as concrete block for the stage, in Area A, has reached eight feet. Lastly, all the footings have been poured--foundation block to follow.
