

# Weekly Blitz

July 28, 2017




## *Pleasant Run Elementary*



In Lower Level B framing was completed, as the HVAC has started. On Main Level A, installation of joist and metal decking for the gym roof finished. The mechanical mezzanine has been poured and concrete block has is two-thirds of the way finished. Finally, concrete block has started on the Main Level of Area B.

# *Taylor Elementary*

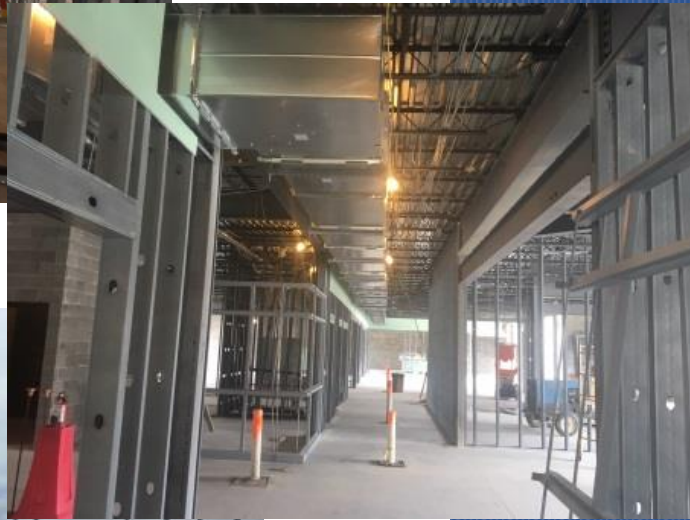

In lower level B main duct work was installed in the corridor along with framing for walls and doors. Pouring for the mezzanine in Area A occurred today. Lastly, the west wall on Main Level B was completed, as the north and east walls are to follow next week.

# Struble Elementary





On Main Level A, the mechanical mezzanine has been prepped for the concrete pour next week. Framing in Lower Level B is nearing completion, while the eastern wing of Main Level B is up to ten feet.

# White Oak Middle School



The new handler in the gym has been installed. Outside, chiller pipe has been placed in the footing: pending tie in. Lastly, new the fan coil units were furnished with coils.

## Bevis Elementary

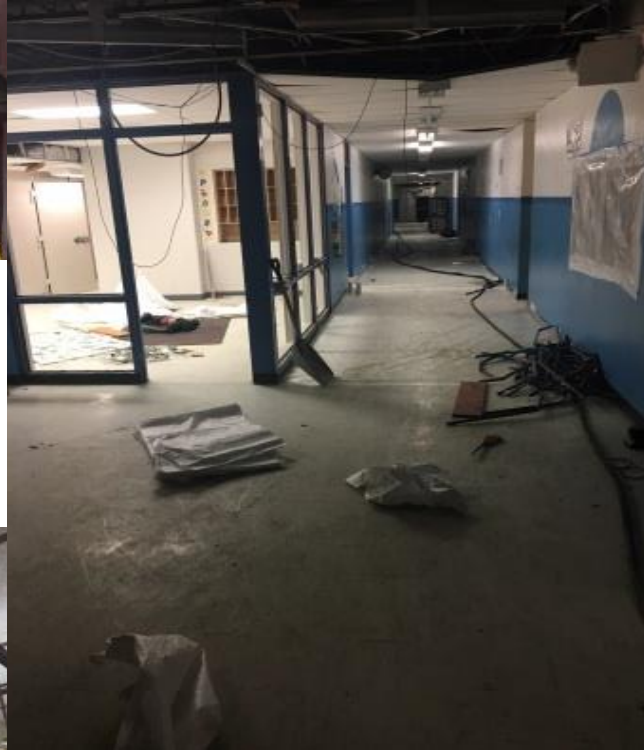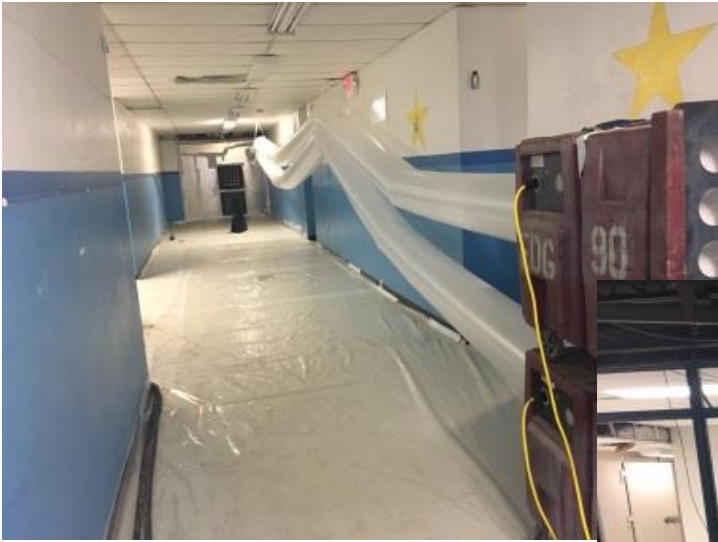

Removal of asbestos in the classrooms and administration area started, as well as the furniture from those areas. Fencing around the perimeter of the school was completed.

# Colerain High School



Brick washing took place on the south, east and southeast elevations.
