

Weekly Blitz - March 31, 2017

Elementary Project Update:

- Rebar was delivered for all three projects this week.



- Footing layout complete for all three projects week for the retaining wall.
- Site utilities continue on all three projects.
- With outlook for weather late Thursday and Friday we are only trying for Struble first concrete pour this week.
- Next week all three projects will be pouring concrete.

Struble Elementary:


- Lower level retaining wall excavated and rebar installed.



- First concrete poured for the lower level retaining wall foundations.



- See the highlighted area below for progress.

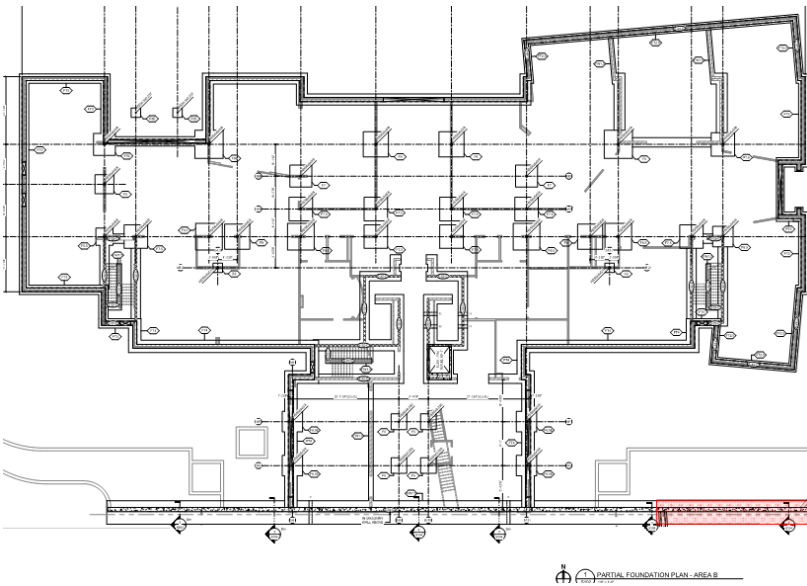

Have a Safe and Happy Spring Break
